

Orange Line Transformation

Construction Project Updates




Week in Review and Lookahead

Friday, October 21, 2022

Work continued to progress this week on [Orange Line Transformation](#) projects, including Traction Power upgrades and construction at Wellington Yard and Vehicle Maintenance Facility



Traction Power Substations

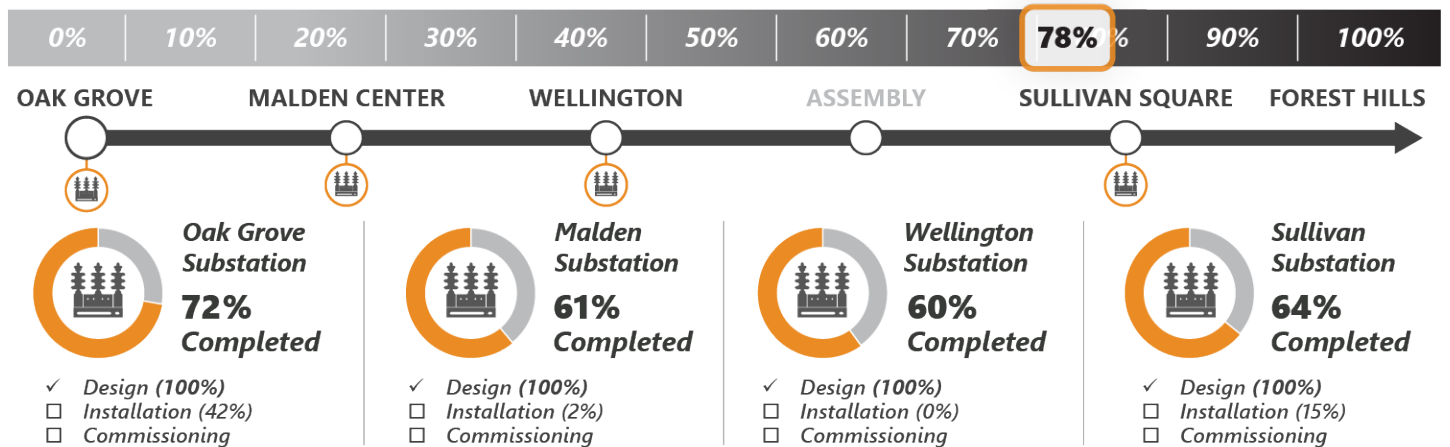

Traction Power Substations: Modernize the third rail power supply to reduce the risk of service disruptions; develop a power system capable of supporting additional Orange Line service

- ✓ **This Week** | Crews continued preparations at Oak Grove for new epoxy flooring installation
- **Lookahead** | Work will progress at Oak Grove on epoxy flooring and conduit installation

Wellington Yard and Maintenance Facility Updates



0% | 10% | 20% | 30% | 40% | 50% | 60% | 70% | 80% | 90% | **96%** | 100%

21,895 Feet of Track



92%
Completed

69 Units of Special Track



85%
Completed

Traction Power & Signals



84%
Completed

Wellington Yard: Upgrade Wellington Yard to increase service capacity, replace outdated infrastructure, and enhance safety.

- ✓ **This Week** | Crews worked on tracks, switch machine and signal testing at the south yard of Wellington
- **Lookahead** | Crews will continue with third rail and switches adjustment and signal testing




0% | 10% | 20% | 30% | 40% | 50% | 60% | 70% | 80% | **87%** | 100%

Building Upgrade



90%
Completed

Power Substation




97%
Completed

Train Wash



82%
Completed

Maintenance Bays



60%
Completed

Wellington Maintenance Facility: Modernize the Vehicle Maintenance Facility to improve vehicle maintenance; reducing customer wait times, provide cleaner cars, and deliver safer operations.

- ✓ **This Week** | Crews performed preparation activities to pour concrete at track 13, electricians are testing fire alarm and working on compressed air in pits at track 14 through 17, painters are performing touchups at different locations at zone 7
- **Lookahead** | Crews will be performing a concrete pour on track 13 and installing vent pipes
